




SECTION 4 - JÁNOVCE - JABLONOV



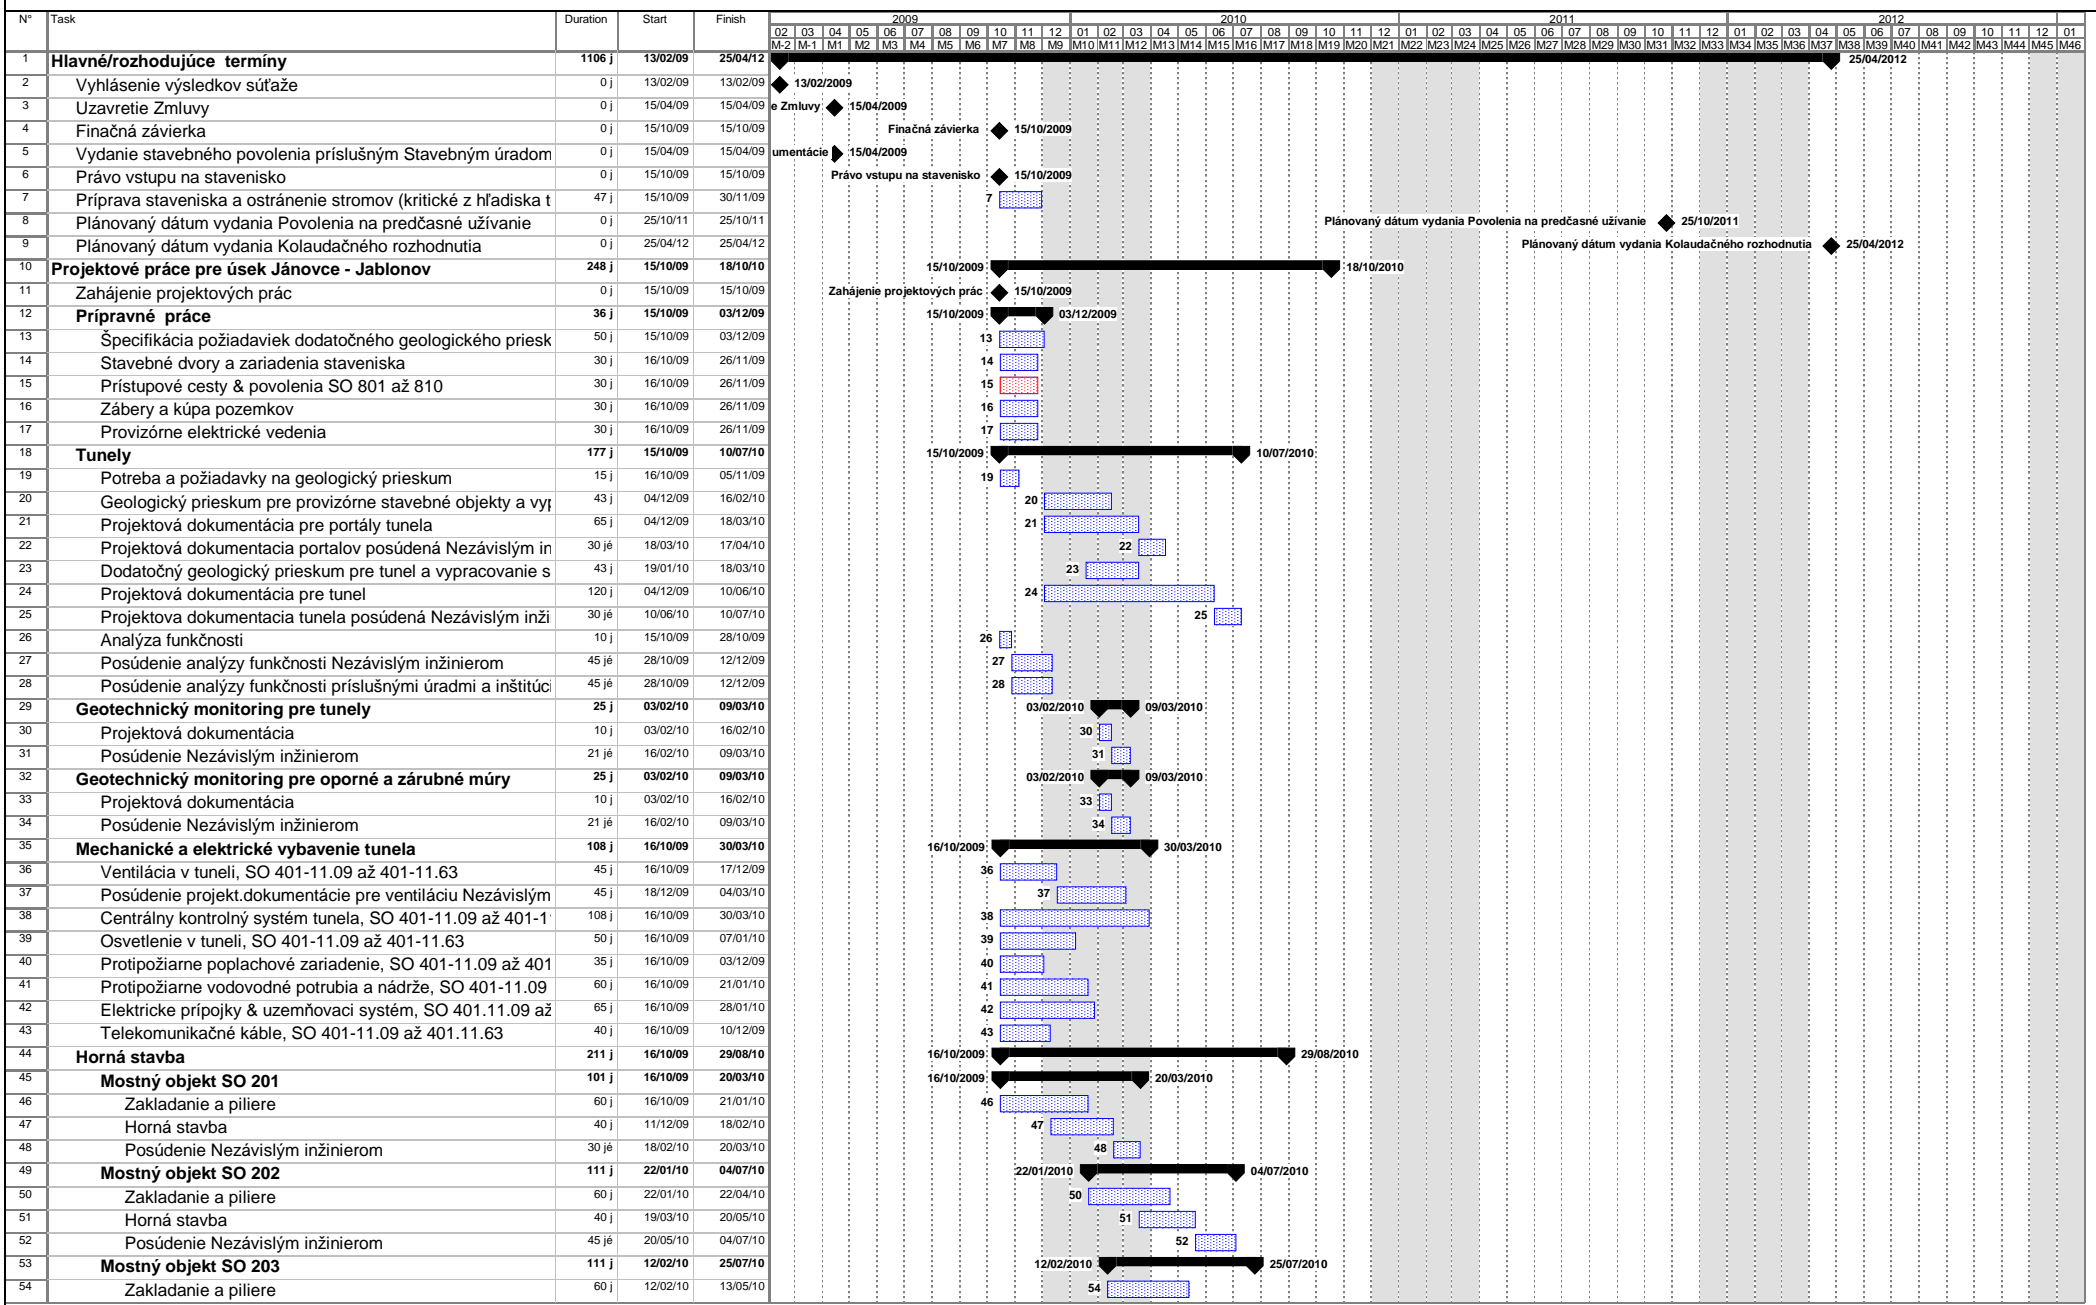


SECTION 4 - JÁNOVCE - JABLONOV

N°	Task	Duration	Start	Finish	2009												2010												2011												2012																	
					02	03	04	05	06	07	08	09	10	11	12	01	02	03	04	05	06	07	08	09	10	11	12	01	02	03	04	05	06	07	08	09	10	11	12	01	02	03	04	05	06	07	08	09	10	11	12	01	02	03	04	05	06	07
109	Mostný objekt SO 216	119 j	16/10/09	18/04/10																																																						
110	Speciálne zakladanie mosta	50 j	16/10/09	07/01/10																																																						
111	Spodna stavba	40 j	27/11/09	04/02/10																																																						
112	Horná stavba	80 j	30/10/09	04/03/10																																																						
113	Posúdenie Nezávislým inžinierom	45 j	04/03/10	18/04/10																																																						
114	Predpokladané schvaľovanie Nezávislým inžinierom pre	45 j	07/01/10	21/02/10																																																						
115	Mostný objekt SO 217	106 j	04/12/09	23/05/10																																																						
116	Zakladanie a piliere	60 j	04/12/09	11/03/10																																																						
117	Horná stavba	40 j	12/02/10	08/04/10																																																						
118	Posúdenie Nezávislým inžinierom	45 j	08/04/10	23/05/10																																																						
119	Predpokladané schvaľovanie Nezávislým inžinierom pre	45 j	11/03/10	25/04/10																																																						
120	Mostný objekt SO 218	111 j	11/12/09	06/06/10																																																						
121	Zaklady mosta, piliere a opory	60 j	11/12/09	18/03/10																																																						
122	Horná stavba	40 j	19/02/10	22/04/10																																																						
123	Posúdenie Nezávislým inžinierom	45 j	22/04/10	06/06/10																																																						
124	Predpokladané schvaľovanie Nezávislým inžinierom pre	45 j	18/03/10	02/05/10																																																						
125	Mostný objekt SO 219	111 j	16/10/09	03/04/10																																																						
126	Zakladanie a piliere	50 j	16/10/09	07/01/10																																																						
127	Speciálne zakladanie	40 j	27/11/09	04/02/10																																																						
128	Horná stavba	80 j	30/10/09	04/03/10																																																						
129	Posúdenie Nezávislým inžinierom	30 j	04/03/10	03/04/10																																																						
130	Mostný objekt SO 220	111 j	05/02/10	18/07/10																																																						
131	Zakladanie a piliere	60 j	05/02/10	06/05/10																																																						
132	Horná stavba	40 j	02/04/10	03/06/10																																																						
133	Posúdenie Nezávislým inžinierom	45 j	03/06/10	18/07/10																																																						
134	Oporné múry SO 229 až 239	114 j	16/10/09	07/04/10																																																						
135	Protihlukové steny/bariéry SO 250 až 254	60 j	08/04/10	07/07/10																																																						
136	Odvodnenie	201 j	16/10/09	13/08/10																																																						
137	Posúdenie Nezávislým inžinierom	87 j	08/04/10	13/08/10																																																						
138	Výkop rýh odvodnenia SO 501	50 j	16/10/09	07/01/10																																																						
139	Pokládka rúrok odvodnenia SO 501	25 j	16/10/09	19/11/09																																																						
140	Výpustný objekt SO 501	25 j	16/10/09	19/11/09																																																						
141	Regulácia prívádzača SO 501	58 j	16/10/09	19/01/10																																																						
142	Úprava potokov & úprava vodných zdrží SO 321 až 328	43 j	16/10/09	15/12/09																																																						
143	Prekládky inžinierskych sietí	247 j	15/10/09	18/10/10																																																						
144	Projekt.dokumentácia a realizácia prekládok rozhodujúcich	240 j	15/10/09	18/10/10																																																						
145	Projekt.dokumentácia a realizácia prekládok ostatných inžin	80 j	22/02/10	18/06/10																																																						
146	Iné práce	178,88 j	16/10/09	18/08/10																																																						
147	Oplotenie SO 301	30 j	08/07/10	18/08/10																																																						
148	Úprava hlavných ciest SO 111 až 113; SO 120 až 135	29 j	16/10/09	25/11/09																																																						
149	Vozovky	50 j	08/04/10	23/06/10																																																						
150	Dopravné značenie	193 j	16/10/09	03/08/10																																																						
151	Informačný systém diaľnice	29 j	16/10/09	25/11/09																																																						
152	Dopravné značky, SO 101 az 142	29 j	24/06/10	03/08/10																																																						
153	MME (Zariadenia pre spravu a údržbu diaľnice)	72 j	26/11/09	19/03/10																																																						
154	Zariadenia pre prevádzku diaľnice	72 j	26/11/09	19/03/10																																																						
155	Verejné obstarávanie	325,13 j	24/01/10	29/12/10																																																						
156	Diaľničná technológia	325,13 j	24/01/10	29/12/10																																																						
157	Cesty	232,13 j	03/05/10	29/12/10																																																						
158	Hlavné káble z optických vlákien	240 j	03/05/10	29/12/10																																																						
159	METEO zariadenia	160 j	03/05/10	10/10/10																																																						
160	CCTV (kamerový systém)	160 j	03/05/10	10/10/10																																																						
161	Hlávka núdzového volania	160 j	03/05/10	10/10/10																																																						
162	Sčítacie zariadenia dopravy	160 j	03/05/10	10/10/10																																																						




SECTION 4 - JÁNNOVCE - JABLONOV

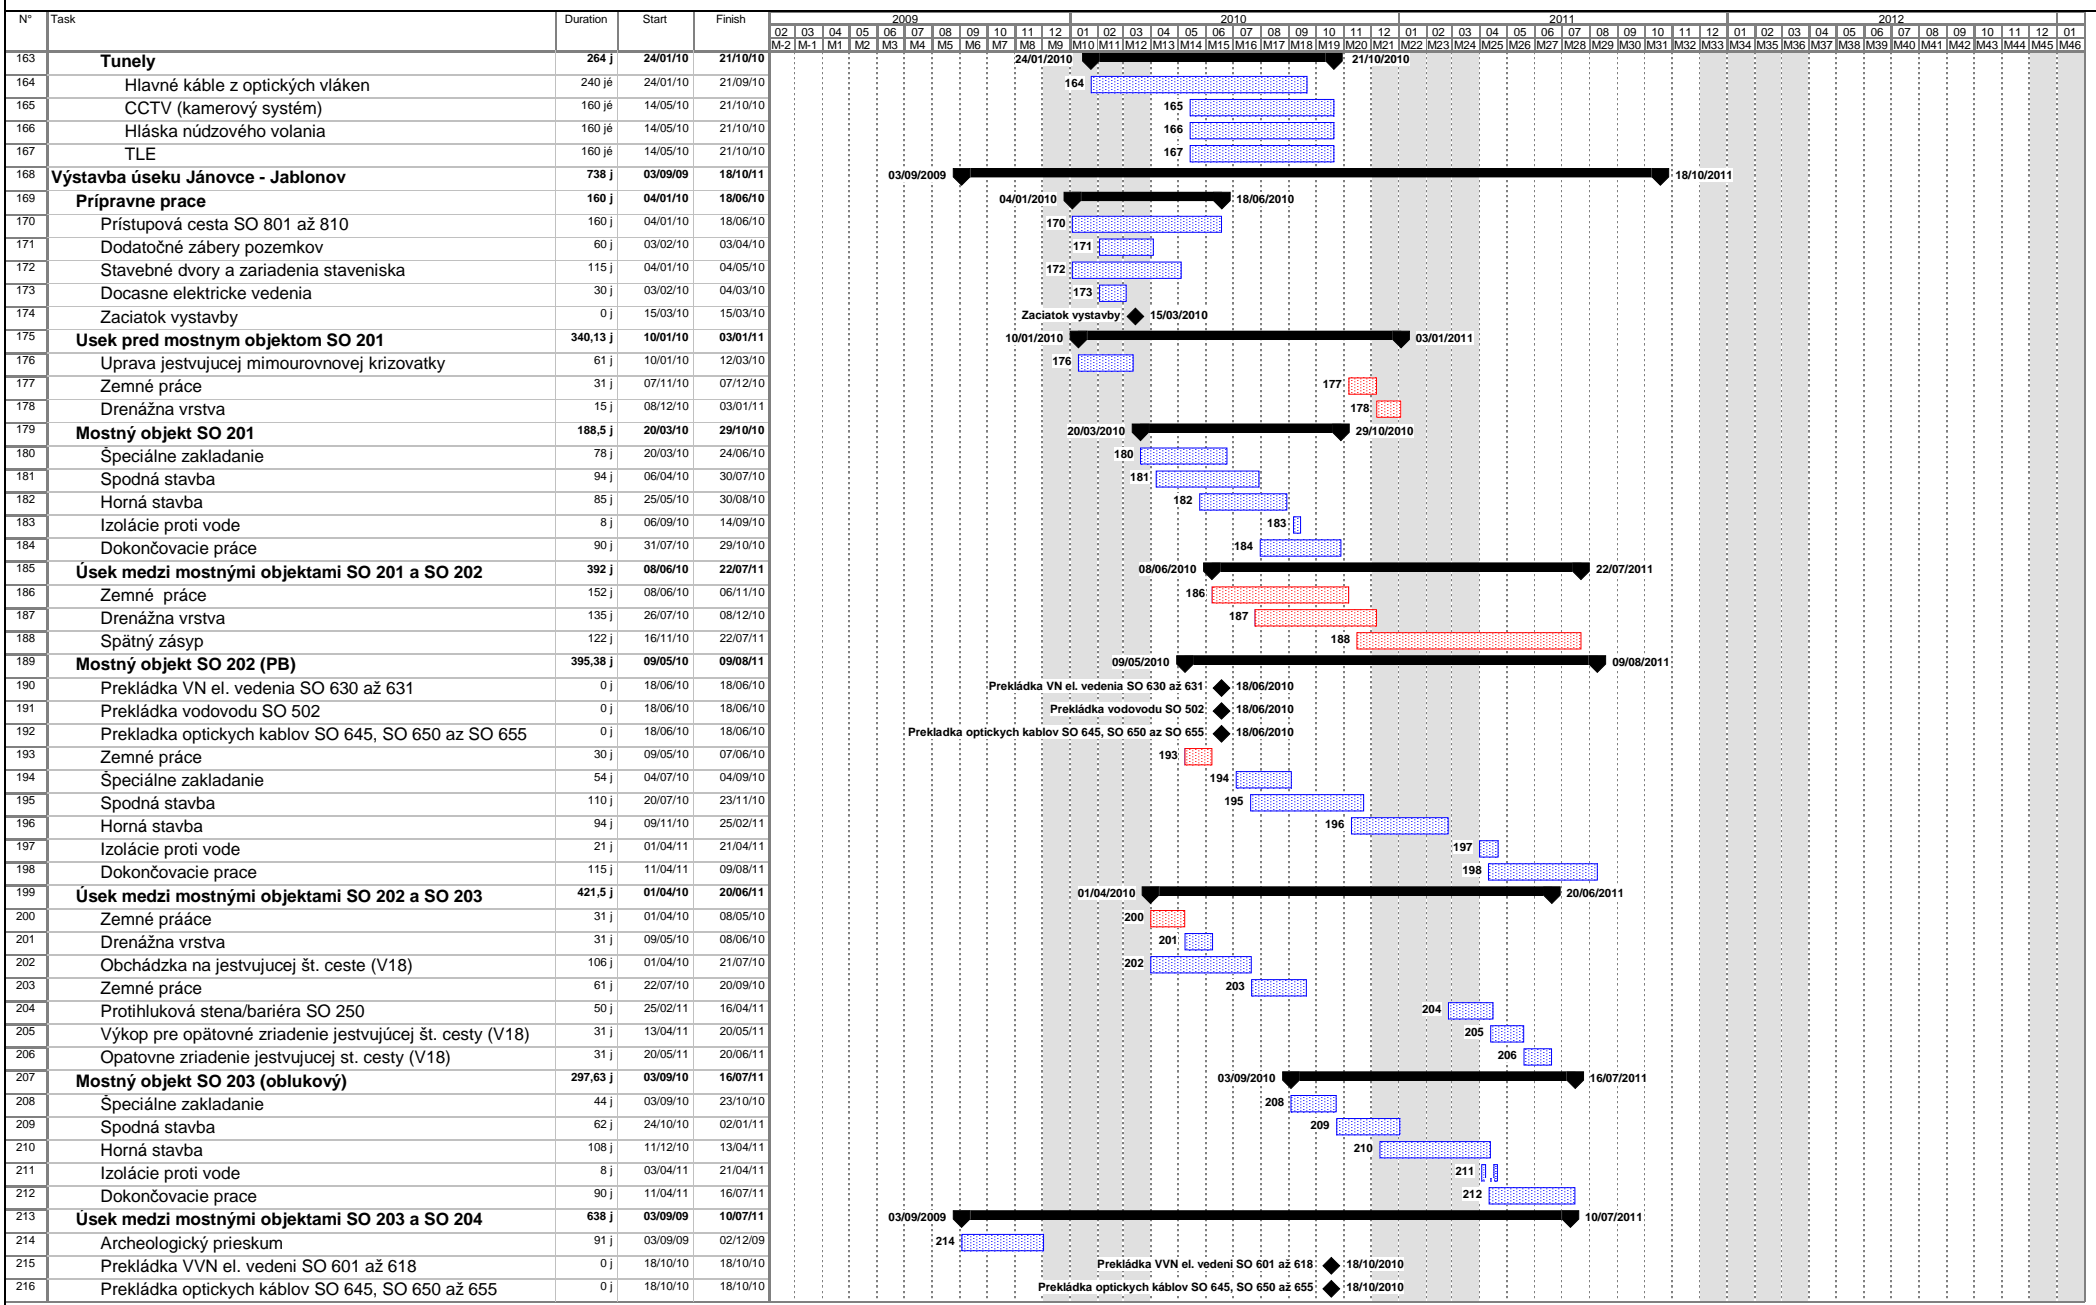



SECTION 4 - JÁNOVCE - JABLONOV

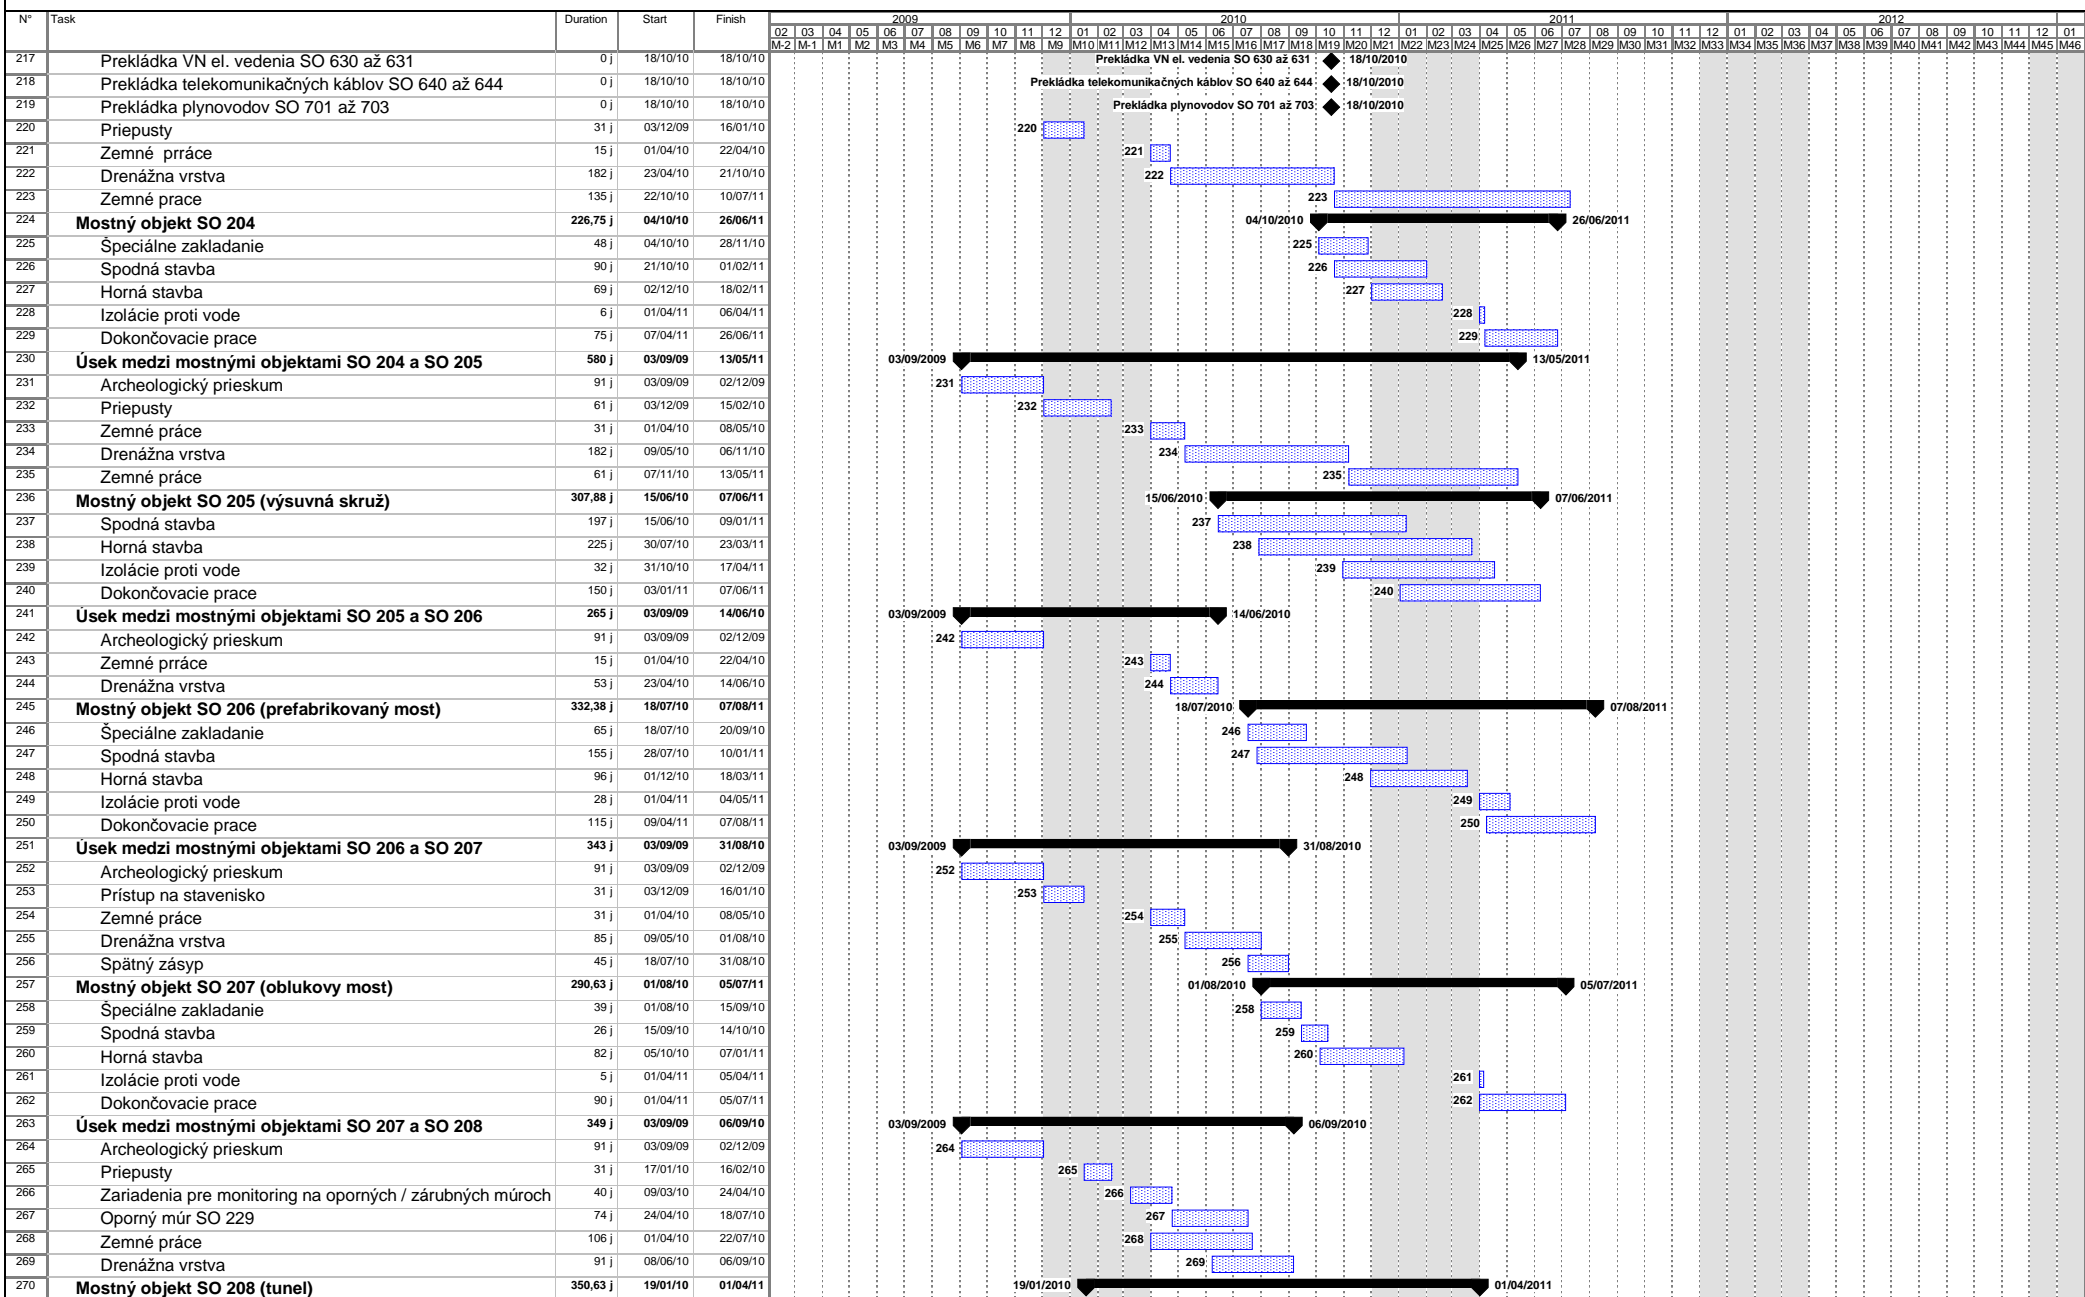



SECTION 4 - JÁNOVCE - JABLONOV

